




Abandoned Mine Reclamation Program PROJECT SUMMARY

PARIA PROJECT Garfield County, Utah AMR/017/909

Project Location and Background

The Paria Project finished up the AML work in the Grand Staircase-Escalante National Monument. Close coordination with the BLM resulted in just one abandoned coal mine site to address. The Little Creek Prospect is located approximately 2 miles west of Henrieville, Utah.

The mine portal was sealed with a solid concrete block wall. Work crews transported all supplies by hand using a 600-foot-long path across the floodplain and up the steep side of the drainage to the portal. The path was then raked out and reseeded. BLM cooperated by granting permission for our improvement and use of the administratively closed road to the project area.

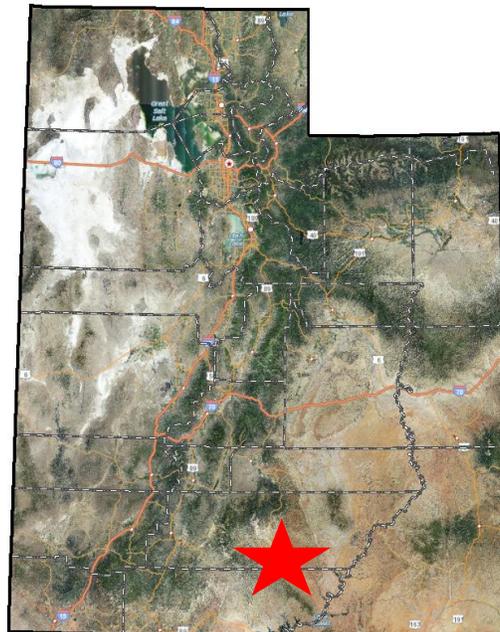

View of pack trail across the floodplain.



Road repair on the way to the project area.



The AMRP in the Division of Oil, Gas and Mining, Utah Department of Natural Resources, was created in 1983 to address physical safety hazards associated with abandoned mines as authorized by the Surface Mining Reclamation and Control Act (SMCRA) of 1977. The Program is funded by The Utah Coal Producers who pay an abandoned mine reclamation fee to the Office of Surface Mining (OSM) on each ton of coal mined in Utah.

Owner:
BLM Grand Staircase-Escalante National Monument

General Contractor:
The 5 Seventeen Company

AMRP Project Manager:
Jan Morse



Abandoned Mine Reclamation Program PROJECT SUMMARY

Paria Project, 2014 -- Construction Summary

The 5 Seventeen Company out of Kamas, Utah was awarded the contract for the project. The work at the site included construction of a solid concrete block wall two courses thick, placed on a concrete footer constructed in the floor of the adit. The access road was repaired on the way in and left in the new condition at the direction of BLM. The temporary foot trail was placed in a location designated by BLM, and removed by raking and seeding after the project work was complete.

**Below: Concrete block wall in progress; Finished wall.
Tag Number 3370130HO1**

PROJECT HIGHLIGHTS:

Project Cost: Bid Amount \$9,815.90
Final Amount **\$9,530.00**

Change Orders: none

Project Dates: Start: June 24, 2014
Finish: June 25, 2014
2 Work Days
2 Calendar Days

Accomplishments: Site Access Improvements: 1
Mine Closure: 1
Revegetation: 0.25 Acres



**Paria Project
AMLIS Key: UT000197
Construction Cost: \$9,530.00**
